BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Yelahanka Division
Project Name	: Improvements to Roads Drains and other developmental works in Ananthapura Attur Ward No 03 under SWM head in Chief Minister Nava Nagarothan grants of yelahanka division Package -08
Consultants	: Rudraprasad Consultants
Project Manager /Team Leader	: Karthik Reehan
Project Start Date	: 29-Apr-20
Project End Date	: 26-Oct-20
Project Length in Months	: 06 months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed	Cum	9070.98	9070.71	100	12-05-20	26-10-20	167
2 a)	Filling in foundation with granite/trap broken metal 100mm and down size, 40mm Jelly	Cum	7.68	7.68	100	17-05-20	26-10-20	162
2 b)	Filling in foundation with granite/trap broken metal 100mm and down size, 20mm Jelly	Cum	7.41	7.41	100	23-05-20	26-10-20	156
2 c)	Filling in foundation with granite/trap broken metal 100mm and down size, Coarse sand.	Cum	5.77	5.77	100	26-05-20	26-10-20	153
2 d)	Filling in foundation with granite/trap broken metal 100mm and down size, Fine Sand	Cum	3.84	3.84	100	28-05-20	26-10-20	151
2 e)	Filling in foundation with granite/trap broken metal 100mm and down size, 12.5mm chips	Cum	5.77	5.77	100	01-06-20	26-10-20	147
4	Providing of Geonets for Rain Water Harvesting pit on top of the filter media as specified and as per the directions of the Engineer-in-charge of the work .	Sqm	19.22	19.22	100	03-06-20	26-10-20	145
5	Providing and laying in position plain cement concrete of Mix 1:3:6 with OPC @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0.892cum and fine aggregates @ 0.465cum machine mixed,	Cum	1411.70	1411.70	100	14-05-20	26-10-20	165
6	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs with 20mm and down size granite metal coarse aggregates at 0.69 cum and fine aggregates at 0.43	Cum	2805.91	2805.91	100	25-05-20	26-10-20	154
7	Providing T.M.T. steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in position, lapping and/or welding wherever required,	Tonne	170.78	170.78	100	19-05-20	26-10-20	160
8	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work	Sqm	198.78	198.78	100	29-05-20	26-10-20	150
9	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting , including form work, cost of alll materials,	Sqm	7511.40	7511.25	100	27-06-20	26-10-20	121

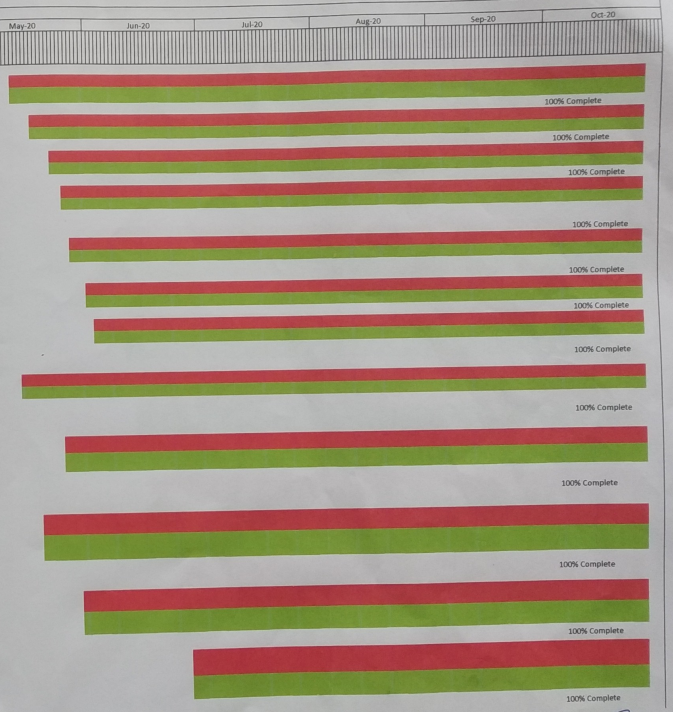

AE

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು - 64

RUDRAPRASAD CONSULTANTS BANGALORE

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Improvements to Roads Drains and other developmental works in Ananthapura Attur Ward No 03 under SWM head in Chief Minister Nava Nagarothan grants of yelahanka division Package -08
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rochan
Project Start Date	:	29-Apr-20
Project End Date	:	26-Oct-20
Project Length in Months	:	06 months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
10	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum,	cum	56.76	56.76	100	01-06-20	26-10-20	147
11	Providing and fixing pre cast solid cement concrete kerb stones made out of C.C. 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3	Nos	6306.00	6305.00	100	03-06-20	26-10-20	145
12	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications. and as per the directions of the Engineer-in-charge of the work .	Sqm	1135.20	1134.86	100	06-06-20	26-10-20	142
13	Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes,	cum	1040.40	375.10	36	12-06-20	26-10-20	136
14	Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications. and as per the directions of the Engineer-in-charge of the work .	Sqm	3468.00	1221.57	35	15-06-20	26-10-20	133
15	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material,	Cum	834.48	296.82	36	18-06-20	26-10-20	130
16	Providing, laying, spreading and compacting cushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site,	Cum	1251.72	280.96	22	25-06-20	26-10-20	123
17	Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM including cleaning of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means	Sqm	5563.20	1221.57	22	29-06-20	26-10-20	119

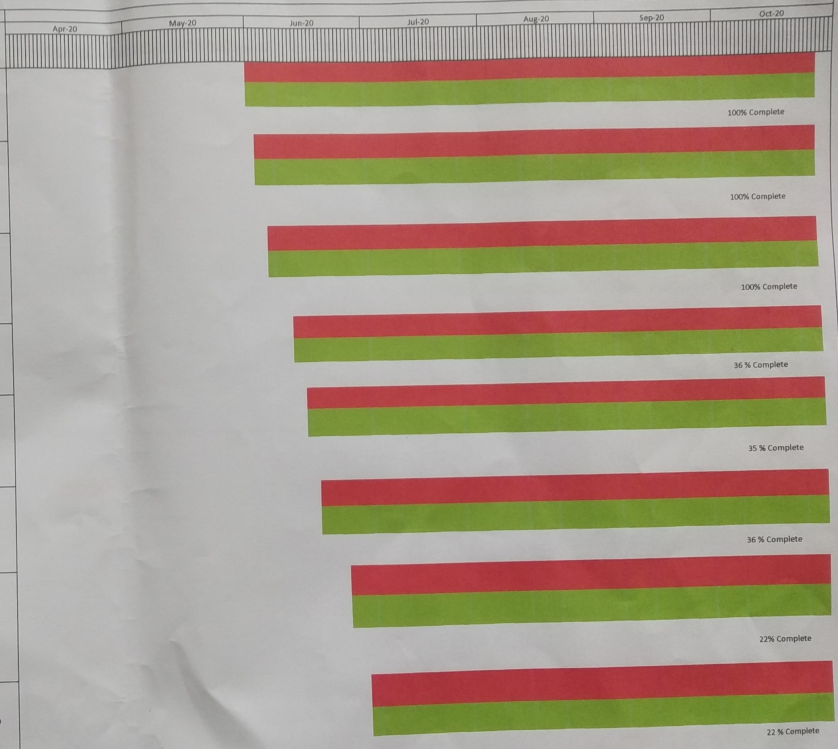

AE

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು - 64

RUDRAPRASAD CONSULTANTS BANGALORE

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Improvements to Roads Drains and other developmental works in Ananthapura Attur Ward No 03 under SWM head in Chief Minister Nava Nagarothan grants of yelahanka division Package -08
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rochan
Project Start Date	:	29-Apr-20
Project End Date	:	26-Oct-20
Project Length in Months	:	06 months

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
18	Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade,	Cum	278.16	61.08	22	29-06-20	26-10-20	119
19	Providing and applying tack coat using 80/100 grade bitumen(VG10) on the prepared black topped surfaces at 2.5 kg per 10 sqm, heating bitumen in boiler fitted with spray set (excluding cleaning of road surface)	Sqm	11629.80	1221.57	11	10-07-20	26-10-20	108
20	Providing and laying bituminous concrete 40mm thick with hot mix plant, using crushed aggregates of specified grading, premixed with bituminous binder and filler, transporting the hot mix to work site,	Cum	430.51	48.86	11	10-07-20	26-10-20	108
21	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface/ Concrete Surface: Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads at 250 gms per sqm area	Sqm	424.40	42	10	23-07-20	26-10-20	95

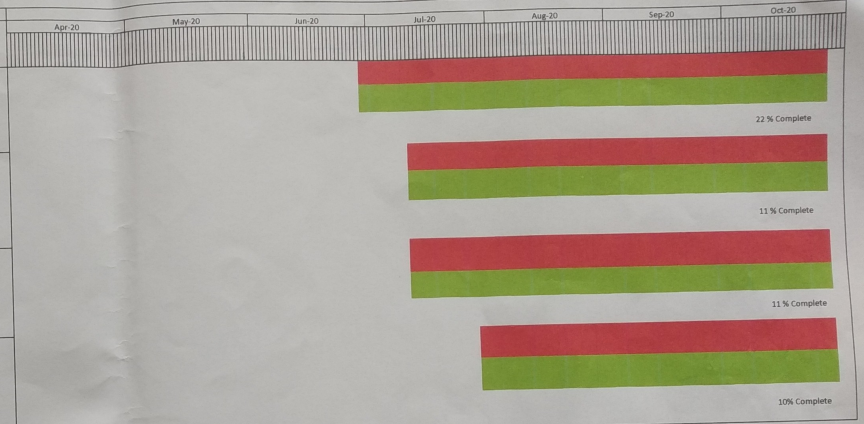

LEGEND

= Planned %

= Executed %

RUDRAPRASAD CONSULTANTS BANGALORE

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು – 64
